CITY OF HAYWARD

AGENDA REPORT

AGENDA DATE 05/03/05

AGENDA ITEM 3

WORK SESSION ITEM _____

TO: Mayor and City Council

FROM: Director of Public Works

SUBJECT: Pavement Rehabilitation Measure B and Gas Tax 2004/05: Award of Contract

RECOMMENDATION:

It is recommended that the City Council adopt the attached resolutions that:

1. Approve Addendum No. 1, which makes minor revisions to the plans and specifications; and
2. Award the contract to G. Bortolotto & Company, Inc., in the amount of $2,092,387.96.

BACKGROUND:

On March 22, 2005, the City Council approved the plans and specifications for the Pavement Rehabilitation Measure B and Gas Tax 2004/05 projects and called for bids to be received on April 19, 2005. During the bidding period, Addendum No. 1 was issued for minor revisions to the plans and specifications, which added additional streets for slurry seal.

These Measure B and Gas Tax funded projects are a continuation of the City's ongoing program to slurry seal residential streets every six-to-seven years to extend the life of the street pavement and to rehabilitate other more heavily traveled streets. Street selection is based on priorities established through the City's Pavement Management Program (PMP). All residential streets in the shaded areas shown in Exhibits A and B are either proposed for slurry seal, dig out, or pavement overlay this year. Also included in the contract is construction of the Measure B funded bicycle lanes on Huntwood Avenue between Olympic Avenue and Folsom Avenue (see Exhibit C).

The selection of streets for rehabilitation is based on staff's analysis of the pavement condition indices identified through the City's computerized PMP, along with specific field examination, and the functional classification of each street. Pavement rehabilitation in this project consists of making deep-lift asphalt concrete spot repairs and placing asphalt concrete overlay on the various streets. Also included are deep-lift asphalt concrete spot repairs throughout the City on various streets that have been identified for localized repair by Streets maintenance staff.

On April 19, 2005, five bids were received for the pavement rehabilitation work. G. Bortolotto & Company, Inc. of San Carlos submitted the low bid in the amount of $2,092,387.96, which is 14.1 percent below the Engineer's Estimate of $2,435,823.00. C.F. Archibald Paving of Redwood City submitted the second low bid in the amount of $2,161,537.40, which is 11.3 percent below the Engineer's Estimate and $69,149.44 more than the low bid. The bids ranged from $2,092,387.96 to $2,738,479.00.

These projects are categorically exempt under the "Operation, Repair, Maintenance, or Minor Alteration of Existing Facilities" section of the California Environmental Quality Act Guidelines.

PROJECT COST:

The estimated project costs are as follows:

Pavement Repair/Rehabilitation – Contract Construction	$ 2,092,388
Detector Loops Replacement	66,000
Re-Striping (City Forces)	70,000
Design and Administration	150,000
Inspection and Testing	178,000
TOTAL	$ 2,556,388

FUNDING:

The 2004-05 Capital Improvement Program includes a total of $1,400,000 in the Measure B Tax Fund (Local Transportation) for the Pavement Rehabilitation 2004/05 project, $1,400,000 in the Gas Tax Fund for the Pavement Rehabilitation 2004/05 project, and $110,000 in the Measure B Tax Fund (Pedestrian & Bicycle) for Huntwood Bicycle Lane Improvement – Olympic to Folsom Avenue project.

SCHEDULE:

Award Contract	May 03, 2005
Begin Work	May 31, 2005
Complete Work	September 23, 2005

Prepared by:

Robert A. Bauman, Deputy Director of Public Works

Recommended by:

for Dennis L. Butler, Director of Public Works

Approved by:

Jesús Armas, City Manager

Attachments: Exhibit A: Project Location Maps
Exhibit B: List of Streets for Slurry Seal, Overlay, and Deep-Lift Patching
Exhibit C: Huntwood Bicycle Lane Improvements
Exhibit D: Summary of Bids

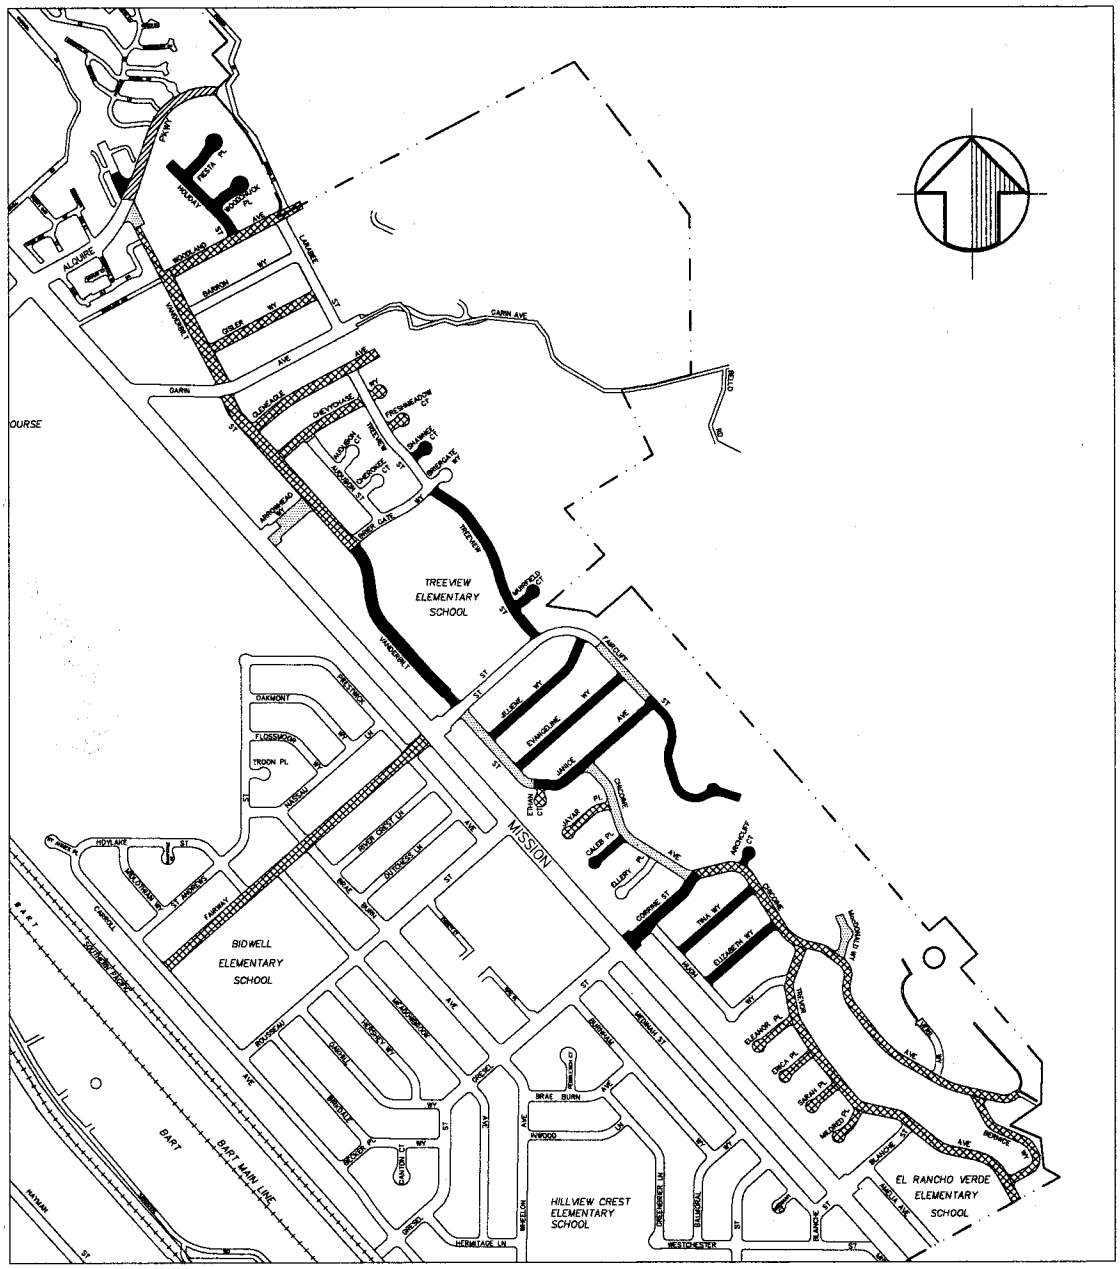

DISTRICT 2

LEGEND

- SPOT REPAIRS AND OVERLAY
- SPOT REPAIRS, GRINDING AND OVERLAY
- SPOT REPAIRS AND SLURRY SEAL
- SPOT REPAIRS ONLY

NOTE:
SEE LIST OF STREETS ON EXHIBIT B

PAVEMENT REHABILITATION MEASURE B PROJECT NO. 5172 OVERLAY LOCATION MAPS

Exhibit A-1

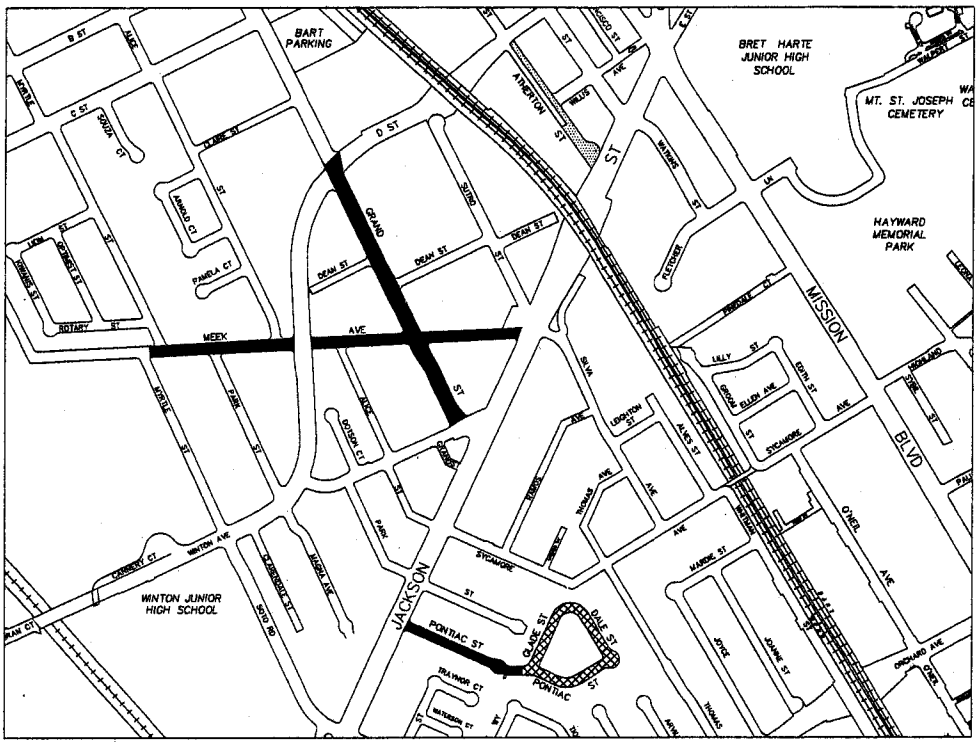

DISTRICTS 19 & 20

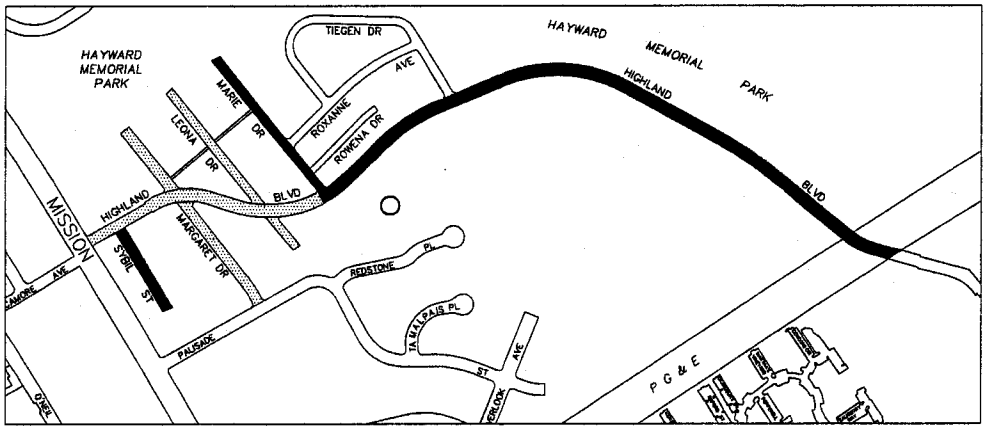

DISTRICT 6

LEGEND

- SPOT REPAIRS AND OVERLAY
- SPOT REPAIRS, GRINDING AND OVERLAY
- SPOT REPAIRS AND SLURRY SEAL

PAVEMENT REHABILITATION
MEASURE B
PROJECT NO. 5172
LOCATION MAPS

NOTE:
SEE LIST OF STREETS ON EXHIBIT B

Exhibit A-2

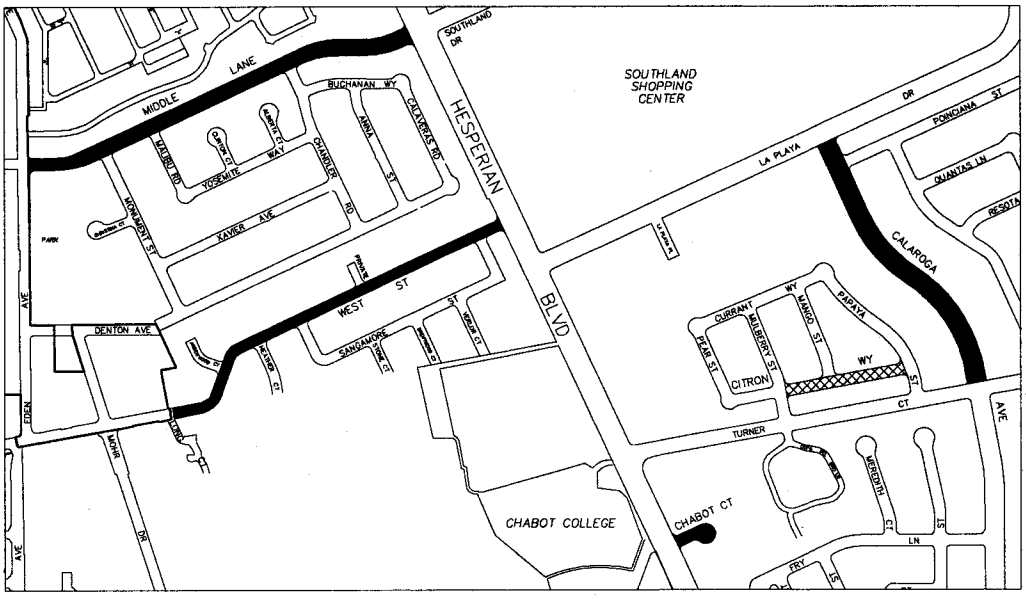

MIDDLE LN, WEST ST, CALAROGA AVE, CHABOT CT & CITRON WY

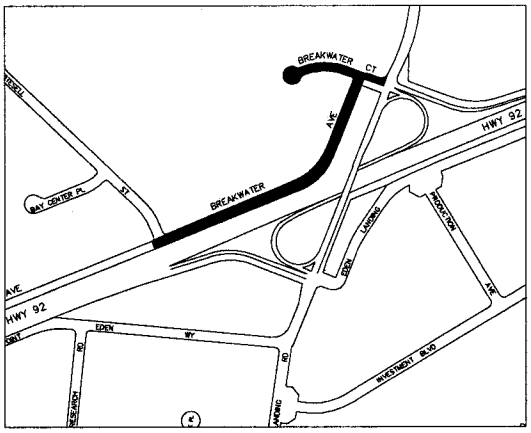

BREAKWATER AVE & BREAKWATER CT

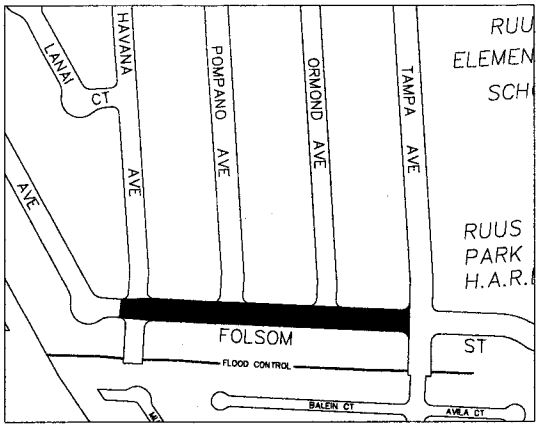

FOLSOM AVE

LEGEND

- SPOT REPAIRS AND OVERLAY
- GRINDING AND OVERLAY
- SPOT REPAIRS AND SLURRY SEAL

PAVEMENT REHABILITATION
GAS TAX
PROJECT NO. 5131
LOCATION MAPS

NOTE:
SEE LIST OF STREETS ON EXHIBIT B

Exhibit A-3

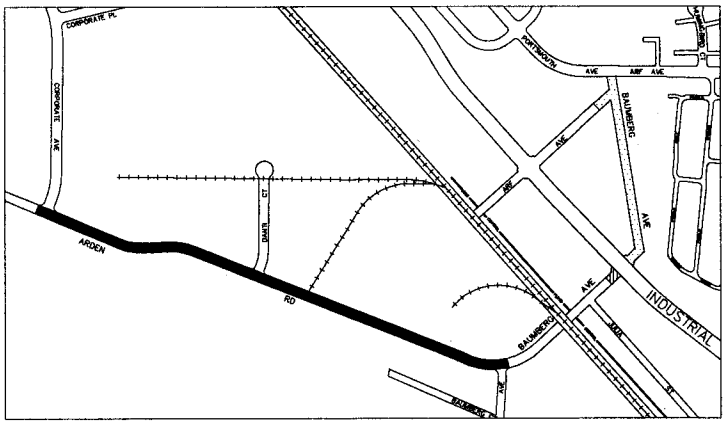

ARDEN RD, BAUMBERG AVE (@ INDUSTRIAL BLVD) &
BAUMBERG AVE (INDUSTRIAL BLVD TO ARF/PORTSMOUTH AVE)

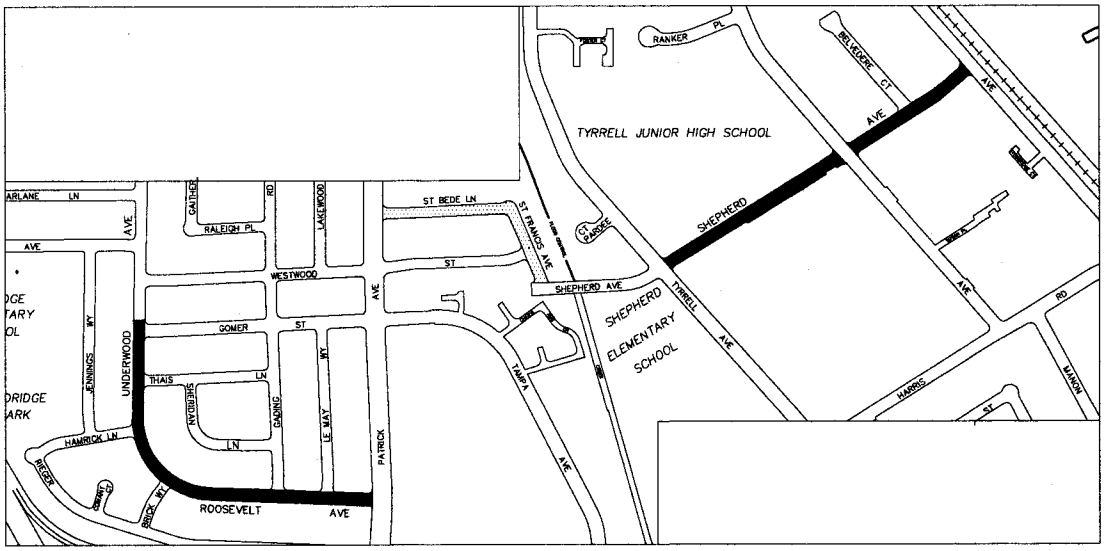

UNDERWOOD AVE, ROOSEVELT AVE,
ST. BEDE LN, ST. FRANCIS AVE, &
SHEPHERD AVE

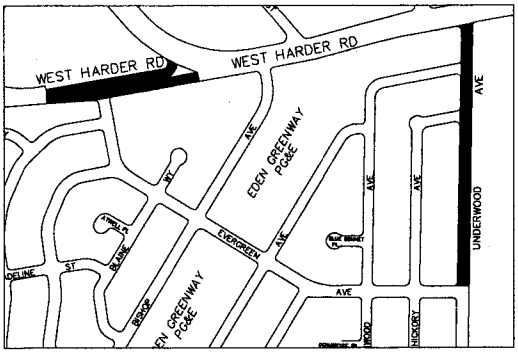

WEST HARDER RD & UNDERWOOD AVE

LEGEND

- SPOT REPAIRS AND OVERLAY
- GRINDING AND OVERLAY
- SPOT REPAIRS AND SLURRY SEAL
- SPOT REPAIRS ONLY

NOTE:
SEE LIST OF STREETS ON EXHIBIT B

PAVEMENT REHABILITATION
GAS TAX
PROJECT NO. 5131
LOCATION MAPS

Exhibit A-4

STREETS FOR OVERLAY (Project 5172)			
	STREET NAME	**FROM**	**TO**
	DISTRICT 2		
1	ARCHCLIFF CT	CHICOINE AV	CUL DE SAC
2	ARROWHEAD WY	MISSION BLVD	VANDERBILT ST
3	AUDUBON ST	CHEVYCHASE WY	34' S/O CHEVYCHASE WY
4	CALEB PL	CHICOINE AV	END
5	CHICOINE AV	JANICE AV	CORRINE ST
6	CORRINE ST	MISSION BLVD	CHICOINE AV
7	ELIZABETH WY	HUGH WY	CHICOINE AV
8	EVANGELINE WY	JANICE AV	FAIRWAY ST
9	FAIRCLIFF ST	JILLIENE WY	EVANGELINE WY
10	FAIRCLIFF ST	EVANGELINE WY	DEAD END
11	FIESTA PL	HOLIDAY ST	END
12	HOLIDAY ST	WOODLAND AV	BARRICADE
13	JANICE AV	ETHAN CT	FAIRCLIFF ST
14	JILLIENE WY	JANICE AV	FAIRWAY ST
15	MACDONALD WY	CHICOINE AV	DEAD END
16	MUIRFIELD CT	TREEVIEW ST	CUL DE SAC
17	SHAWNEE CT	TREEVIEW ST	CUL DE SAC
18	TINA WY	HUGH WY	CHICOINE AV
19	TREEVIEW ST	FAIRWAY ST	BRIERGATE WY
20	VANDERBILT ST	ALQUIRE PKWY	130' TOWARD BARRICADE
21	VANDERBILT ST	ETHAN CT	FAIRWAY ST
22	VANDERBILT ST	FAIRWAY ST	BRIERGATE WY
23	VANDERBILT ST	WOODLAND AV	ALQUIRE PKWY
24	WOODCHUCK PL	HOLIDAY ST	CUL DE SAC
	DISTRICT 6		
25	HIGHLAND BLVD	MISSION BLVD	MARIE DR
26	HIGHLAND BLVD	MARIE DR	END @ BARRICADE
27	SYBIL ST	HIGHLAND BLVD	BARRICADE
28	MARGARET DR	PALISADE ST	DEAD END
29	LEONA DR	200' S/O HIGHLAND BLVD	END
30	MARIE DR	HIGHLAND BLVD	DEAD END
	DISTRICTS 19 & 20		
31	ATHERTON ST	D ST	END
32	GRAND AV	WINTON AV	D ST
33	MEEK AV	D ST	MYRTLE ST
34	MEEK AV	JACKSON ST	D ST
35	PONTIAC ST	JACKSON ST	DALE ST

Exhibit B-1

STREETS FOR SLURRY SEAL (Project 5172)			
	STREET NAME	**FROM**	**TO**
	DISTRICT 2		
1	BERNICE WY	TREVOR AV	CHICOINE AV
2	CHEVYCHASE WY	VANDERBILT ST	DEAD END
3	CHICOINE AV	CORRINE ST	END
4	ELEANOR PL	TREVOR AV	END
5	ERICA PL	CUL DE SAC	TREVOR AV
6	ETHAN CT	JANICE AV	END
7	FAIRWAY ST	BRAE BURN AV	MISSION BLVD
8	FAIRWAY ST	CARROLL AV	BRAE BURN AV
9	FRESHMEADOW CT	TREEVIEW ST	CUL DE SAC
10	GISLER WY	VANDERBILT ST	LARRABEE ST
11	GLENEAGLE AV	VANDERBILT ST	DEAD END
12	JAYAR PL	CHICOINE AV	END
13	MILDRED PL	CUL DE SAC	TREVOR AV
14	SARAH PL	TREVOR AV	END
15	TREVOR AV	CHICOINE AV	MILDRED PL
16	TREVOR AV	MILDRED PL	END
17	VANDERBILT ST	BRIERGATE WY	125' S/O ALQUIRE PKWY
18	WOODLAND AV	VANDERBILT ST	END @ BARRICADE
	DISTRICTS 6, 19 & 20		
19	PONTIAC ST	GLADE AV	DALE ST
20	GLADE ST	PONTIAC ST	DALE ST
21	DALE ST	PONTIAC ST	GLADE ST

STREETS FOR DEEP-LIFT STREET PATCHING (Project 5172)			
	STREET NAME	**FROM**	**TO**
1	ALQUIRE PKWY	VANDERBILT ST	AT BARRICADE

ADDITIONAL STREETS FOR OVERLAY (Project 5131)			
	STREET NAME	**FROM**	**TO**
	OTHER STREETS		
1	ARDEN RD	CORPORATE AV	BAUMBERG CT
2	BAUMBERG AV	ARF/PORTSMOUTH AV	INDUSTRIAL PKWY
3	BREAKWATER AV	CLAWITER RD	WHITESELL ST
4	BREAKWATER CT	CUL-DE-SAC	CLAWITER RD
5	CALAROGA AV	TURNER CT	LA PLAYA DR
6	CHABOT CT	HESPERIAN BLVD	CUL DE SAC
7	FOLSOM AV	HAVANA AV	TAMPA AV
8	MIDDLE LN	EDEN AV	HESPERIAN BLVD
9	ROOSEVELT AV	PATRICK AV	BRICK WY
10	SHEPHERD AV	TYRRELL AV	HUNTWOOD AV
11	ST. BEDE LN	PATRICK AV	ST. FRANCIS AV
12	ST. FRANCIS AV	SHEPHERD AV	ST. BEDE LN
13	UNDERWOOD AV	HARDER RD	PVMNT CHG @ EVERGREEN ST
14	UNDERWOOD AV	PVMNT CHG @ GOMER ST	PVMNT CHG @ BRICK WY
15	WEST HARDER RD	SANTA CLARA ST	172' W/O EVERGREEN ST
16	WEST ST	LONG CT	HESPERIAN BLVD

STREETS FOR SLURRY SEAL (Project 5131)			
	STREET NAME	**FROM**	**TO**
1	CITRON WY	MULBERRY ST	PAPAYA ST

STREETS FOR DEEP-LIFT STREET PATCHING (Project 5131)			
	STREET NAME	**FROM**	**TO**
1	BAUMBERG AV	INDUSTRIAL PKWY	ARDEN RD

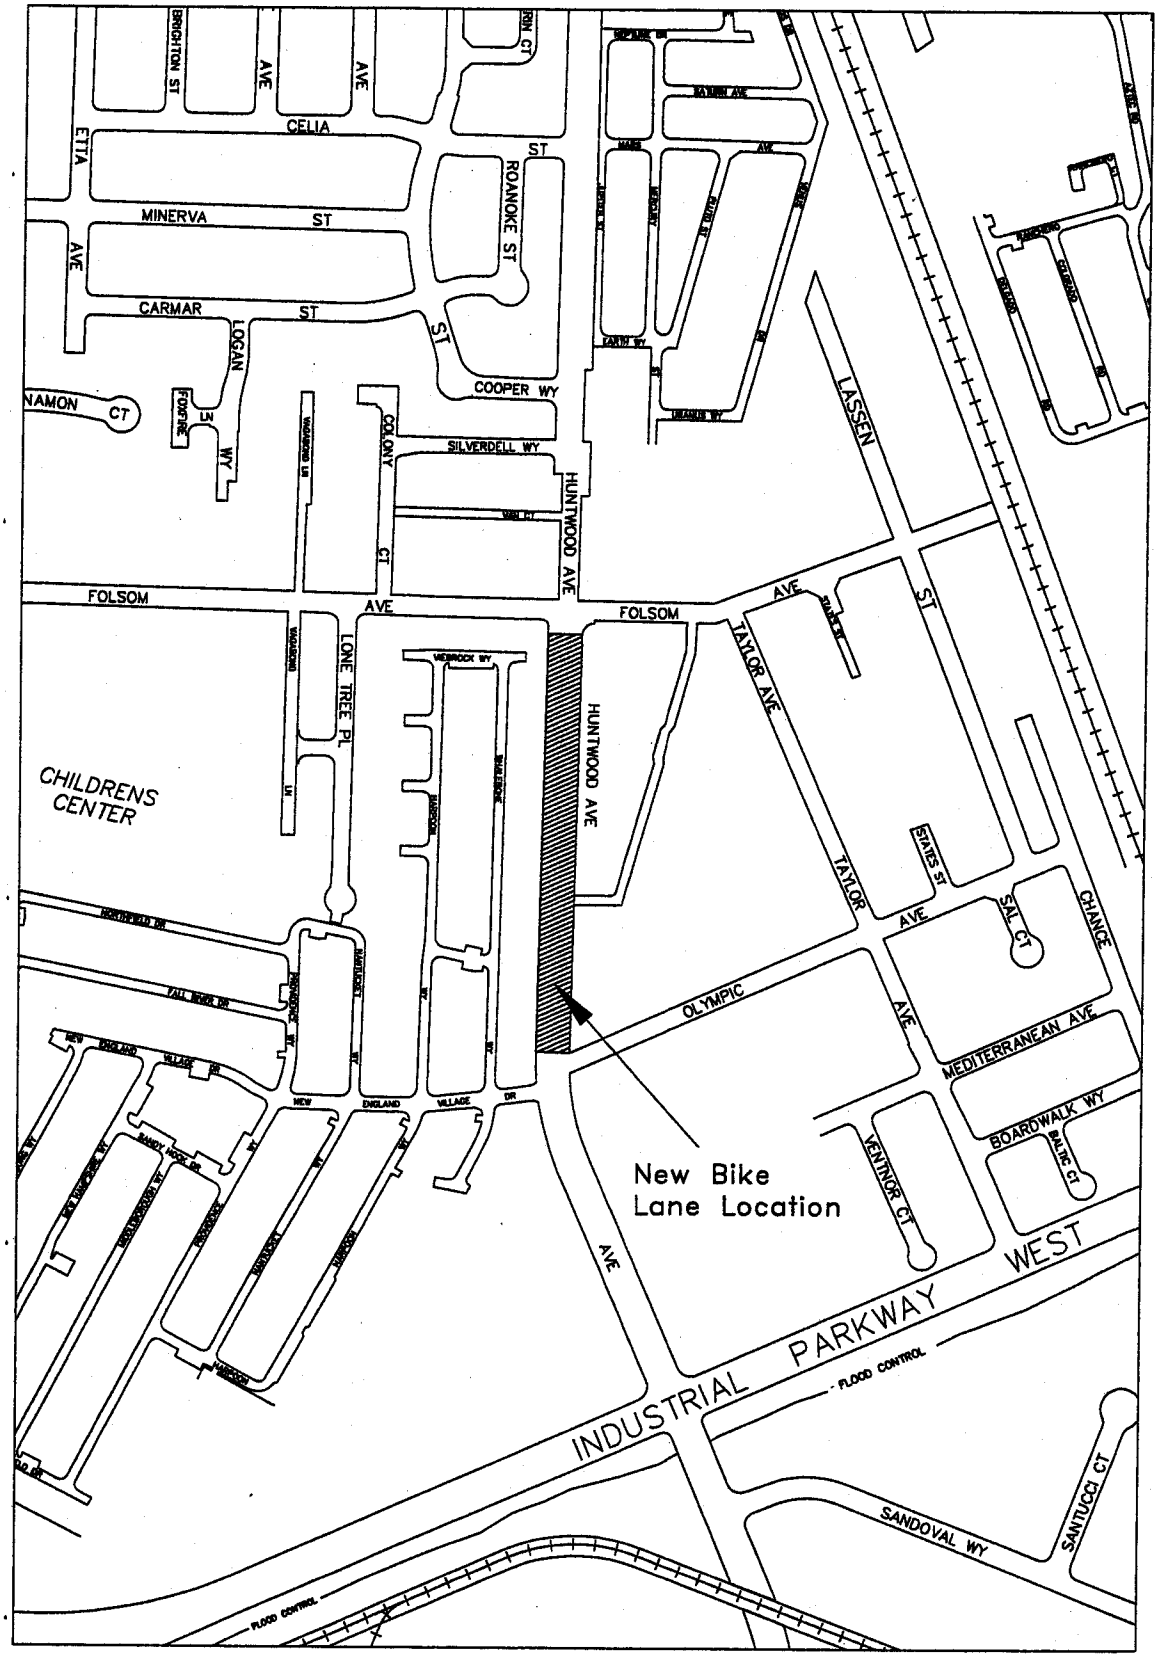

LOCATION MAP

Huntwood Bicycle Lane Improvement

Exhibit C-1

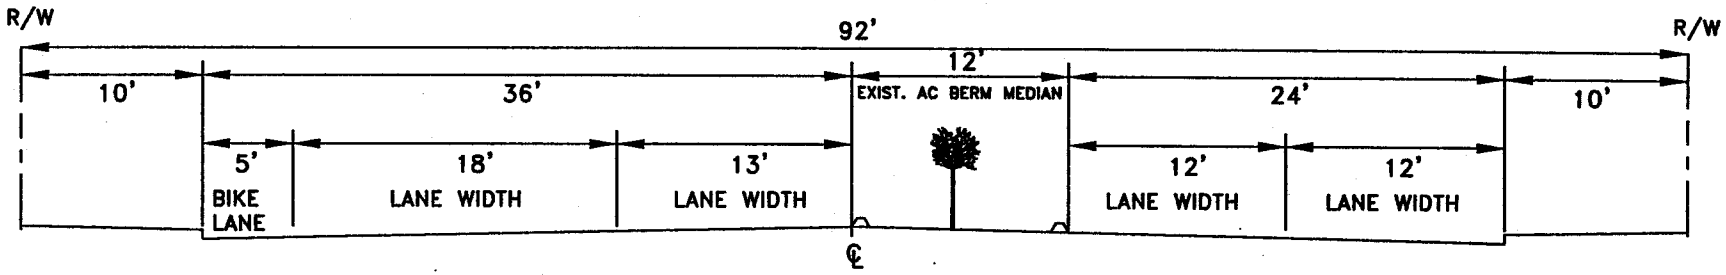

EXISTING STREET SECTION
HUNTWOOD AVE

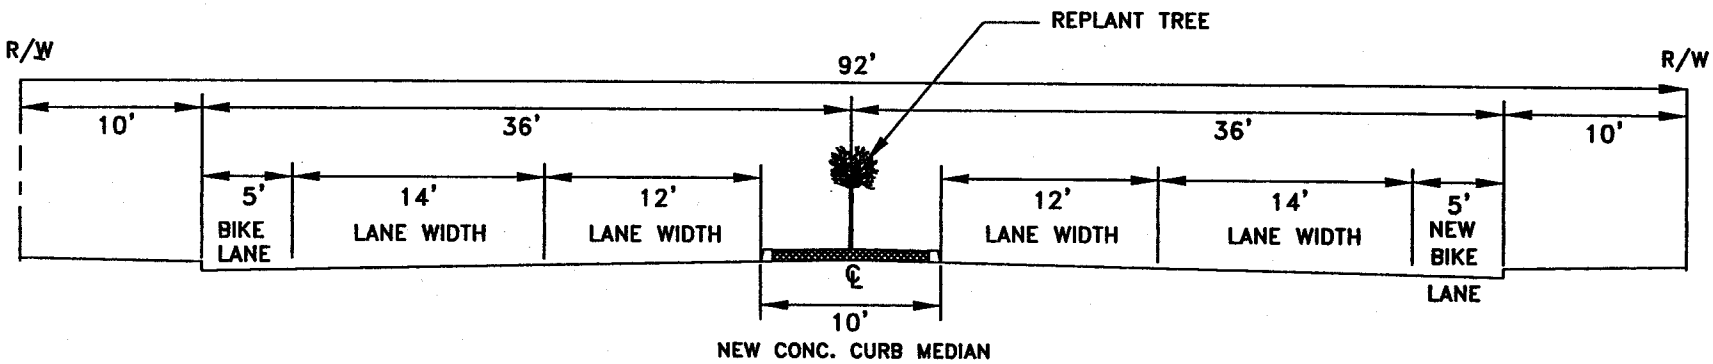

NEW CROSS SECTION
HUNTWOOD AVE

HUNTWOOD BICYCLE LANE IMPROVEMENT

Exhibit C-2

CITY OF HAYWARD
PAVEMENT REHABILITATION MEASURE B AND GAS TAX 2004/05
PROJECT NO. 5131, 5172, AND 5174
BIDS OPENED: APRIL 19, 2005

(NUMBER OF BIDS RECEIVED - 5)

BID SUMMARY				ENGINEER'S ESTIMATE		G. Bortolotto & Company Inc. 580 Bragato Road San Carlos, CA 94070-6227 (650) 595-2591 PHONE (650) 595-0718 FAX		C. F. Archibald Paving Inc. 3624 Haven Avenue Redwood City, CA 94064 (650) 364-3045 PHONE (650) 366-8777 FAX		Desilva Gates Construction 11555 Dublin Blvd Dublin, CA 94568 (925) 829-9220 PHONE (925) 803-4263 FAX	
ITEM	QUANTITY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
			SCHEDULE A (PROJ. NO. 5131)								
1	1	LS	TRAFFIC CONTROL	5,000.00	5,000.00	54,151.00	54,151.00	20,000.00	20,000.00	49,000.00	49,000.00
2	7	EA	REMOVE & REPLACE SPEED HUMP	2,000.00	14,000.00	1,700.00	11,900.00	1,500.00	10,500.00	1,000.00	7,000.00
3	2,259	SY	SLURRY SEAL	0.70	1,581.30	2.91	6,573.69	3.00	6,777.00	2.00	4,518.00
4	9,735	TON	ASPHALT CONCRETE OVERLAY	55.00	535,425.00	45.54	443,331.90	49.90	485,776.50	48.00	467,280.00
5	1,634	SF	4" DEEPLIFT AC SPOT REPAIR (S/S AREAS)	2.50	4,085.00	2.89	4,722.26	2.20	3,594.80	2.00	3,268.00
6	83,209	SF	4" DEEPLIFT AC SPOT REPAIR (O/L AREAS)	2.50	208,022.50	1.99	165,585.91	2.20	183,059.80	2.50	208,022.50
7	42,128	SF	6" DEEPLIFT AC SPOT REPAIR	3.50	147,448.00	2.89	121,749.92	2.90	122,171.20	3.25	136,916.00
8	6,416	SY	PLANE PAVEMENT (0.15' FULL WIDTH)	3.00	19,248.00	1.53	9,816.48	1.90	12,190.40	2.00	12,832.00
9	27,535	SY	PLANE PAVEMENT (6' WEDGE CUT)	2.00	55,070.00	1.19	32,766.65	1.20	33,042.00	1.20	33,042.00
10	1,295	SY	PLANE PAVEMENT (10' CONFORM CUT)	2.00	2,590.00	1.53	1,981.35	2.00	2,590.00	2.00	2,590.00
11	88	EA	ADJUST WATER VALVE BOX & COVER TO GRADE	150.00	13,200.00	100.00	8,800.00	90.00	7,920.00	225.00	19,800.00
12	46	EA	REPLACE WATER VALVE BOX & COVER TO GRADE	250.00	11,500.00	200.00	9,200.00	200.00	9,200.00	250.00	11,500.00
13	18	EA	ADJUST SURVEY MONUMENT BOX & COVER TO GRADE	200.00	3,600.00	100.00	1,800.00	110.00	1,980.00	225.00	4,050.00
14	30	EA	REPLACE SURVEY MONUMENT BOX, COVER, & ADJUST TO GRADE	275.00	8,250.00	200.00	6,000.00	220.00	6,600.00	250.00	7,500.00
15	81	EA	ADJUST MANHOLE FRAME & COVER TO GRADE	275.00	22,275.00	201.00	16,281.00	200.00	16,200.00	325.00	26,325.00
16	7	EA	ADJUST SEWER RISER BOX & COVER TO GRADE	250.00	1,750.00	201.00	1,407.00	230.00	1,610.00	250.00	1,750.00
			SUBTOTAL - SCHEDULE A		**1,053,044.80**		**896,067.16**		**923,211.70**		**995,393.50**

Exhibit D

CITY OF HAYWARD
PAVEMENT REHABILITATION MEASURE B AND GAS TAX 2004/05
PROJECT NO. 5131, 5172, AND 5174
BIDS OPENED: APRIL 19, 2005

(NUMBER OF BIDS RECEIVED - 5)

BID SUMMARY				ENGINEER'S ESTIMATE		G. Bortolotto & Company Inc. 580 Bragato Road San Carlos, CA 94070-6227 (650) 595-2591 PHONE (650) 595-0718 FAX		C. F. Archibald Paving Inc. 3624 Haven Avenue Redwood City, CA 94064 (650) 364-3045 PHONE (650) 366-8777 FAX		Desilva Gates Construction 11555 Dublin Blvd Dublin, CA 94568 (925) 829-9220 PHONE (925) 803-4263 FAX	
ITEM	QUANTITY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
			SCHEDULE B (PROJECT NO. 5172)								
17	1	LS	TRAFFIC CONTROL	5,000.00	5,000.00	54,151.00	54,151.00	25,000.00	25,000.00	50,000.00	50,000.00
18	27,000	SF	REMOVE ASPHALT CONCRETE (APPROX. 1" IN GUTTER)	1.00	27,000.00	0.49	13,230.00	0.50	13,500.00	0.40	10,800.00
19	67,617	SY	SLURRY SEAL	0.70	47,331.90	0.61	41,246.37	0.60	40,570.20	0.60	40,570.20
20	10,001	TON	ASPHALT CONCRETE OVERLAY	55.00	550,055.00	45.54	455,445.54	49.90	499,049.90	48.00	480,048.00
21	20,129	SF	4" DEEPLIFT AC SPOT REPAIR	2.50	50,322.50	1.99	40,056.71	2.20	44,283.80	2.00	40,258.00
22	20,489	SF	6" DEEPLIFT AC SPOT REPAIR (S/S AREAS)	3.50	71,711.50	3.01	61,671.89	3.00	61,467.00	3.25	66,589.25
23	16,824	SF	6" DEEPLIFT AC SPOT REPAIR (O/L AREAS)	3.50	58,884.00	2.89	48,621.36	2.90	48,789.60	3.25	54,678.00
24	12,461	SY	PLANE PAVEMENT (0.10' FULL WIDTH)	2.00	24,922.00	1.33	16,573.13	1.00	12,461.00	1.50	18,691.50
25	4,994	SY	PLANE PAVEMENT (0.15' FULL WIDTH)	3.00	14,982.00	1.60	7,990.40	1.50	7,491.00	2.00	9,988.00
26	6,629	SY	PLANE PAVEMENT (0.20' FULL WIDTH)	3.00	19,887.00	1.79	11,865.91	2.00	13,258.00	2.50	16,572.50
27	24,611	SY	PLANE PAVEMENT (6' WEDGE CUT)	2.00	49,222.00	1.19	29,287.09	1.20	29,533.20	1.20	29,533.20
28	1,840	SY	PLANE PAVEMENT (10' CONFORM CUT)	2.00	3,680.00	1.53	2,815.20	2.00	3,680.00	2.00	3,680.00
29	126	EA	ADJUST WATER VALVE BOX & COVER TO GRADE	150.00	18,900.00	100.00	12,600.00	90.00	11,340.00	225.00	28,350.00
30	50	EA	REPLACE WATER VALVE, COVER, & ADJUST TO GRADE	250.00	12,500.00	200.00	10,000.00	220.00	11,000.00	250.00	12,500.00
31	33	EA	ADJUST SURVEY MONUMENT BOX & COVER TO GRADE	200.00	6,600.00	100.00	3,300.00	110.00	3,630.00	235.00	7,755.00
32	34	EA	REPLACE SURVEY MONUMENT BOX & COVER & ADJUST TO GRADE	275.00	9,350.00	200.00	6,800.00	220.00	7,480.00	250.00	8,500.00
33	117	EA	ADJUST MANHOLE FRAME & COVER TO GRADE	275.00	32,175.00	201.00	23,517.00	200.00	23,400.00	325.00	38,025.00

CITY OF HAYWARD
PAVEMENT REHABILITATION MEASURE B AND GAS TAX 2004/05
PROJECT NO. 5131, 5172, AND 5174
BIDS OPENED: APRIL 19, 2005

(NUMBER OF BIDS RECEIVED - 5)

BID SUMMARY				ENGINEER'S ESTIMATE		G. Bortolotto & Company Inc. 580 Bragato Road San Carlos, CA 94070-6227 (650) 595-2591 PHONE (650) 595-0718 FAX		C. F. Archibald Paving Inc. 3624 Haven Avenue Redwood City, CA 94064 (650) 364-3045 PHONE (650) 366-8777 FAX		Desilva Gates Construction 11555 Dublin Blvd Dublin, CA 94568 (925) 829-9220 PHONE (925) 803-4263 FAX	
ITEM	QUANTITY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
34	16	EA	ADJUST SEWER RISER BOX & COVER TO GRADE	250.00	4,000.00	100.00	1,600.00	220.00	3,520.00	250.00	4,000.00
35	1	EA	ADJUST CALTRANS LID BOX	335.00	335.00	310.00	310.00	400.00	400.00	1,000.00	1,000.00
			SUBTOTAL - SCHEDULE B		**1,006,857.90**		**841,081.60**		**859,853.70**		**921,538.65**
			SCHEDULE C (PROJECT NO. 5174)								
36	1	LS	TRAFFIC CONTROL	1,000.00	1,000.00	4,000.00	4,000.00	5,000.00	5,000.00	5,000.00	5,000.00
37	960	LF	REMOVE AND CONSTRUCT MEDIAN	65.00	62,400.00	55.00	52,800.00	68.00	65,280.00	60.00	57,600.00
38	6,720	SF	6" DEEPLIFT AC SPOT REPAIR	3.50	23,520.00	3.01	20,227.20	3.60	24,192.00	3.25	21,840.00
			SUBTOTAL - SCHEDULE C		**86,920.00**		**77,027.20**		**94,472.00**		**84,440.00**
39	1	LS	CRACK SEAL	40,000.00	40,000.00	30,000.00	30,000.00	35,000.00	35,000.00	26,000.00	26,000.00
40	1	LS	RECYCLING IMPLEMENTATION	1,000.00	1,000.00	212.00	212.00	1,000.00	1,000.00	1,000.00	1,000.00
41	1	LS	ADMINISTRATIVE CHANGE ORDERS	248,000.00	248,000.00	248,000.00	248,000.00	248,000.00	248,000.00	248,000.00	248,000.00
			TOTAL		**2,435,822.70**		**2,092,387.96**		**2,161,537.40**		**2,276,372.15**

CITY OF HAYWARD
PAVEMENT REHABILITATION MEASURE B AND GAS TAX 2004/05
PROJECT NO. 5131, 5172, AND 5174
BIDS OPENED: APRIL 19, 2005

(NUMBER OF BIDS RECEIVED - 5)

BID SUMMARY				ENGINEER'S ESTIMATE		O'Grady Paving Inc. 2513 Wyandotte Street Mountain View, CA 94043 (650) 966-1926 PHONE (650) 966-1946 FAX		Granite Construction Company 715 Comstock Street Santa Clara, CA 950543403 (831) 724-1011 PHONE (831) 768-4021 FAX	
ITEM	QUANTITY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
			SCHEDULE A (PROJ. NO. 5131)						
1	1	LS	TRAFFIC CONTROL	5,000.00	5,000.00	41,500.00	41,500.00	8,200.00	8,200.00
2	7	EA	REMOVE & REPLACE SPEED HUMP	2,000.00	14,000.00	2,500.00	17,500.00	1,700.00	11,900.00
3	2,259	SY	SLURRY SEAL	0.70	1,581.30	1.00	2,259.00	2.00	4,518.00
4	9,735	TON	ASPHALT CONCRETE OVERLAY	55.00	535,425.00	50.20	488,697.00	60.00	584,100.00
5	1,634	SF	4" DEEPLIFT AC SPOT REPAIR (S/S AREAS)	2.50	4,085.00	5.00	8,170.00	3.00	4,902.00
6	83,209	SF	4" DEEPLIFT AC SPOT REPAIR (O/L AREAS)	2.50	208,022.50	2.00	166,418.00	3.00	249,627.00
7	42,128	SF	6" DEEPLIFT AC SPOT REPAIR	3.50	147,448.00	3.00	126,384.00	4.00	168,512.00
8	6,416	SY	PLANE PAVEMENT (0.15' FULL WIDTH)	3.00	19,248.00	2.20	14,115.20	2.00	12,832.00
9	27,535	SY	PLANE PAVEMENT (6' WEDGE CUT)	2.00	55,070.00	1.40	38,549.00	2.00	55,070.00
10	1,295	SY	PLANE PAVEMENT (10' CONFORM CUT)	2.00	2,590.00	3.30	4,273.50	2.00	2,590.00
11	88	EA	ADJUST WATER VALVE BOX & COVER TO GRADE	150.00	13,200.00	200.00	17,600.00	270.00	23,760.00
12	46	EA	REPLACE WATER VALVE BOX & COVER TO GRADE	250.00	11,500.00	250.00	11,500.00	350.00	16,100.00
13	18	EA	ADJUST SURVEY MONUMENT BOX & COVER TO GRADE	200.00	3,600.00	200.00	3,600.00	270.00	4,860.00
14	30	EA	REPLACE SURVEY MONUMENT BOX, COVER, & ADJUST TO GRADE	275.00	8,250.00	230.00	6,900.00	350.00	10,500.00
15	81	EA	ADJUST MANHOLE FRAME & COVER TO GRADE	275.00	22,275.00	260.00	21,060.00	400.00	32,400.00
16	7	EA	ADJUST SEWER RISER BOX & COVER TO GRADE	250.00	1,750.00	200.00	1,400.00	510.00	3,570.00
			SUBTOTAL - SCHEDULE A		**1,053,044.80**		**969,925.70**		**1,193,441.00**

CITY OF HAYWARD
PAVEMENT REHABILITATION MEASURE B AND GAS TAX 2004/05
PROJECT NO. 5131, 5172, AND 5174
BIDS OPENED: APRIL 19, 2005

(NUMBER OF BIDS RECEIVED - 5)

BID SUMMARY				ENGINEER'S ESTIMATE		O'Grady Paving Inc. 2513 Wyandotte Street Mountain View, CA 94043 (650) 966-1926 PHONE (650) 966-1946 FAX		Granite Construction Company 715 Comstock Street Santa Clara, CA 950543403 (831) 724-1011 PHONE (831) 768-4021 FAX	
ITEM	QUANTITY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
			SCHEDULE B (PROJECT NO. 5172)						
17	1	LS	TRAFFIC CONTROL	5,000.00	5,000.00	41,500.00	41,500.00	5,000.00	5,000.00
18	27,000	SF	REMOVE ASPHALT CONCRETE (APPROX. 1" IN GUTTER)	1.00	27,000.00	0.50	13,500.00	0.50	13,500.00
19	67,617	SY	SLURRY SEAL	0.70	47,331.90	1.00	67,617.00	1.00	67,617.00
20	10,001	TON	ASPHALT CONCRETE OVERLAY	55.00	550,055.00	50.20	502,050.20	61.00	610,061.00
21	20,129	SF	4" DEEPLIFT AC SPOT REPAIR	2.50	50,322.50	2.50	50,322.50	3.00	60,387.00
22	20,489	SF	6" DEEPLIFT AC SPOT REPAIR (S/S AREAS)	3.50	71,711.50	3.10	63,515.90	4.00	81,956.00
23	16,824	SF	6" DEEPLIFT AC SPOT REPAIR (O/L AREAS)	3.50	58,884.00	3.10	52,154.40	4.00	67,296.00
24	12,461	SY	PLANE PAVEMENT (0.10' FULL WIDTH)	2.00	24,922.00	1.55	19,314.55	2.00	24,922.00
25	4,994	SY	PLANE PAVEMENT (0.15' FULL WIDTH)	3.00	14,982.00	2.10	10,487.40	2.00	9,988.00
26	6,629	SY	PLANE PAVEMENT (0.20' FULL WIDTH)	3.00	19,887.00	2.50	16,572.50	2.00	13,258.00
27	24,611	SY	PLANE PAVEMENT (6' WEDGE CUT)	2.00	49,222.00	1.45	35,685.95	2.00	49,222.00
28	1,840	SY	PLANE PAVEMENT (10' CONFORM CUT)	2.00	3,680.00	3.50	6,440.00	2.00	3,680.00
29	126	EA	ADJUST WATER VALVE BOX & COVER TO GRADE	150.00	18,900.00	200.00	25,200.00	270.00	34,020.00
30	50	EA	REPLACE WATER VALVE, COVER, & ADJUST TO GRADE	250.00	12,500.00	250.00	12,500.00	350.00	17,500.00
31	33	EA	ADJUST SURVEY MONUMENT BOX & COVER TO GRADE	200.00	6,600.00	200.00	6,600.00	270.00	8,910.00
32	34	EA	REPLACE SURVEY MONUMENT BOX & COVER & ADJUST TO GRADE	275.00	9,350.00	230.00	7,820.00	350.00	11,900.00
33	117	EA	ADJUST MANHOLE FRAME & COVER TO GRADE	275.00	32,175.00	260.00	30,420.00	510.00	59,670.00

CITY OF HAYWARD
PAVEMENT REHABILITATION MEASURE B AND GAS TAX 2004/05
PROJECT NO. 5131, 5172, AND 5174
BIDS OPENED: APRIL 19, 2005

(NUMBER OF BIDS RECEIVED - 5)

BID SUMMARY				ENGINEER'S ESTIMATE		O'Grady Paving Inc. 2513 Wyandotte Street Mountain View, CA 94043 (650) 966-1926 PHONE (650) 966-1946 FAX		Granite Construction Company 715 Comstock Street Santa Clara, CA 950543403 (831) 724-1011 PHONE (831) 768-4021 FAX	
ITEM	QUANTITY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
34	16	EA	ADJUST SEWER RISER BOX & COVER TO GRADE	250.00	4,000.00	200.00	3,200.00	510.00	8,160.00
35	1	EA	ADJUST CALTRANS LID BOX	335.00	335.00	500.00	500.00	510.00	510.00
			SUBTOTAL - SCHEDULE B		**1,006,857.90**		**965,400.40**		**1,147,557.00**
			SCHEDULE C (PROJECT NO. 5174)						
36	1	LS	TRAFFIC CONTROL	1,000.00	1,000.00	11,835.60	11,835.60	1,000.00	1,000.00
37	960	LF	REMOVE AND CONSTRUCT MEDIAN	65.00	62,400.00	90.00	86,400.00	85.00	81,600.00
38	6,720	SF	6" DEEPLIFT AC SPOT REPAIR	3.50	23,520.00	2.80	18,816.00	4.00	26,880.00
			SUBTOTAL - SCHEDULE C		**86,920.00**		**117,051.60**		**109,480.00**
39	1	LS	CRACK SEAL	40,000.00	40,000.00	30,654.43	30,654.43	40,000.00	40,000.00
40	1	LS	RECYCLING IMPLEMENTATION	1,000.00	1,000.00	2,000.00	2,000.00	1.00	1.00
41	1	LS	ADMINISTRATIVE CHANGE ORDERS	248,000.00	248,000.00	248,000.00	248,000.00	248,000.00	248,000.00
			TOTAL		**2,435,822.70**		**2,333,032.13**		**2,738,479.00**

DRAFT

HAYWARD CITY COUNCIL

RESOLUTION NO. 05-

Introduced by Council Member_____

RESOLUTION AWARDING CONTRACT TO
G. BORTOLOTTO & COMPANY, INC., FOR THE PAVEMENT
REHABILITATION MEASURE B AND GAS TAX 2004/05
PROJECT, PROJECT NOS. 5131, 5172 AND 5174

WHEREAS, on March 22, 2005, the City Council approved the plans and specifications for the Pavement Rehabilitation Measure B and Gas Tax 2004/05 Project, Project Nos. 5131, 5172 and 5174 and called for bids to be received on April 19, 2005; and

WHEREAS, on April 19, 2005, five bids were received ranging from $2,092,387.96 to $2,738,479.00; G. Bortolotto & Company, Inc., of San Carlos submitted the low bid in the amount of $2,092,387.96 which is approximately 14.1 percent below the Engineer's estimate of $2,435,823.00.

NOW, THEREFORE, BE IT RESOLVED that G. Bortolotto & Company, Inc., is hereby awarded the contract for the Pavement Rehabilitation Measure B and Gas Tax 2004/05 Project, Project Nos. 5131, 5172 and 5174, in accordance with the plans and specifications adopted therefor and on file in the office of the City Clerk of the City of Hayward, at and for the price named and stated in the bid of the hereinabove specified bidder, and all other bids are hereby rejected.

BE IT FURTHER RESOLVED that the City Manager is hereby authorized and directed to execute the contract with G. Bortolotto & Company, Inc., in the name of and for and on behalf of the City of Hayward, in an amount not to exceed $2,092,387.96, in a form to be approved by the City Attorney.

IN COUNCIL, HAYWARD, CALIFORNIA_____, 2005

ADOPTED BY THE FOLLOWING VOTE:

AYES: COUNCIL MEMBERS:
MAYOR:

NOES: COUNCIL MEMBERS:

ABSTAIN: COUNCIL MEMBERS:

ABSENT: COUNCIL MEMBERS:

ATTEST:_____
City Clerk of the City of Hayward

APPROVED AS TO FORM:

_____
City Attorney of the City of Hayward
